


# WASATCH TRAILS FOUNDATION TAP GRANT

MIA YUE, EXECUTIVE DIRECTOR



# WASATCH TRAILS FOUNDATION

2025 Year-End TAP Report Midway City



## TRAIL CREW STATS

- Total Trail Crew Cost:
  - \$120,228.81
- Total Trail Crew Hours:
  - 2,730
- Total Volunteer Hours:
  - 559+



## MAJOR ACCOMPLISHMENTS FOR THE CREW

- WOWZA, Boulder Dash, Tall T
- WHOA!!! Trail
- Dutch Hollow Restoration
- WildWood Development



# TRAIL AREAS MAINTAINED SUMMER 2025

## WASATCH MOUNTAIN STATE PARK

- DUTCH HOLLOW
- PINE CANYON EAST
- PINE CANYON WEST
- WOW/MAPLE GROVE
- WOWZA/TALL T CONNECTOR
- SIDS



## JORDANELLE STATE PARK

### HIDEOUT AREA TRAILS

### JORDANELLE RIDGE TRAIL SYSTEM

- WILE E CANYON TRAILHEAD
- UVU TRAILHEAD



## BIG POLE HOA

### BLUE SAGE RANCH

### RED LEDGES (PUBLIC TRAIL)


### WILDWOOD/BENLOCK



# REPORTS - TRAILFORKS

## Work Per Riding Area (Paid)

- Wasatch Mountain State Park
- Dutch Hollow in Wasatch Mountain State Park
- Jordanelle Ridge Trail System
- Soldier Hollow
- Jordanelle Reservoir

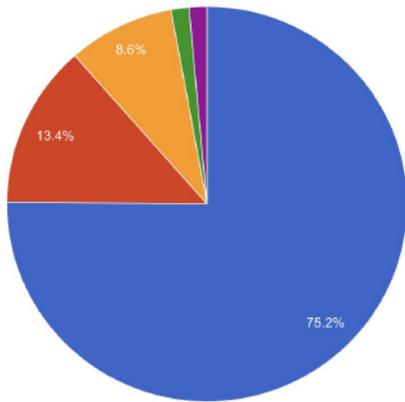

✗	Visitor's Center Ret...	Wasatch Mountai...	Oct 9, 2025	hike Touch up, drainage, rock stairs at top entrance. Tool removal, project complete. <b>P</b>	Unknown	view	40
✗	Visitor's Center Ret...	Wasatch Mountai...	Oct 8, 2025	mtb Benching and trail tread construction. <b>P</b>	Unknown	view	30
✗	Visitor's Center Ret...	Wasatch Mountai...	Oct 7, 2025	mtb Corridor cut all the way through with chainsaw. Bench constructed for top 1/2. <b>P</b>	Unknown	view	40
✗	Whoa!!!	Wasatch Mountai...	Oct 6, 2025	mtb Construction of new "B" route, ride around for canyon gap. Rebuild of step up lip at toilet bowl. Rebuild of bench and lip before Nascar Turns. Rebuild of entrance to final 5 double line. Saw work, root touch up. <b>P</b>	Unknown	view	35
✓	Bike Park Exit	Wasatch Mountai...	Oct 1, 2025	mtb Full trail tread raked, loose rocks removed.	Dry	view	4
✓	Hot Dogger	Wasatch Mountai...	Oct 1, 2025	mtb Full trail tread raked out, loose rocks removed, lips for jump and rollers all tuned up from the meadow to the bottom. New side lips added to remaining table tops that did not previously have them.	Dry	view	36
✓	Hot Dogger	Wasatch Mountai...	Sep 30, 2025	mtb Full trail tread raked out, loose rocks removed, lips for jump and rollers all tuned up from top of trail to the meadow.	Dry	view	40
✓	WOW (Wasatch Ov...	Wasatch Mountai...	Sep 29, 2025	mtb Blown out corner exits and benching repaired above Maple Grove. Cornering support added.	Dry	view	30
✗	Whoa!!!	Wasatch Mountai...	Sep 29, 2025	mtb Temporary signage added. Trail rating and description at top. Individual hazard areas and features all marked. <b>P</b>	Unknown	view	5
✗	Visitor's Center Ret...	Wasatch Mountai...	Sep 25, 2025	mtb Initial flagging. <b>P</b>	Unknown	view	20

